

Work Order ID 136767***136767***

Page 1

Friday, September 04, 2015 10:06:15 AM

Item ID: D6101-017 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Saddle Billet
Start Date: 9/4/2015 Start Qty: 10.00 ***10*** Cust Item ID:
Required Date: 9/4/2015 Req'd Qty: 10.00 ***10*** Customer:
Reference:

Approvals: Process Plan: MCS Date: SEP 04 2015 Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D6101	B

100		0.00
-----	--	------

100

Purchasing

Purchasing

PURCHASING

Memo

Issue P/O: 29713

a) Description: Alluminum billet

b) 6.350" x 6.250" x 2.250" thick (+0.030 / -0.000)

c) Tolerance on all dimensions are +0.030"/-0.000"

d) Grain direction along 6.350" length

e) Material: 7075-T7351 (QQ-A-250/12)

f) Material certification required

CX

SEP 08 2015

10

110

Receive & Inspect for Damage & Mat'l Certs

0.00

110

Packaging

Packaging

Memo

Ensure material certification is attached

10X SP15-09-23

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : ☐			

Work Order ID 136767

136767

Page 2

Friday, September 04, 2015 10:06:15 AM

Item ID: D6101-017 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Saddle Billet
 Start Date: 9/4/2015 Start Qty: 10.00 *10* Cust Item ID:
 Required Date: 9/4/2015 Req'd Qty: 10.00 *10* Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC6- Inspect dimensions to drawing	0.00							
120						10	0		DAS 14 9-89 15/09/24
QC	Memo	0.00							
Quality Control	Ensure Material certification comply to Dwg D6101								
130	Identify as per dwg & Stock Location: MAT044	0.00							
130						10	0		DAS 14 9-89 15/09/24
Packaging	Memo	0.00							
Packaging	LOCATION: MAT044								
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.00							
Quality Control									

20150924

SA

DQA: _____ Date: _____




WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width: 100%; border: none;"> <tr> <td style="border: none;">Skid-tube ☐</td> <td style="border: none;">Cross tube ☐</td> <td style="border: none;">Water Jet ☐</td> <td style="border: none;">Engineering ☐</td> </tr> <tr> <td style="border: none;">Machining ☐</td> <td style="border: none;">Small Fab ☐</td> <td style="border: none;">Prod. Eng. Coord. ☐</td> <td style="border: none;">Quality ☐</td> </tr> <tr> <td style="border: none;">Thermoforming ☐</td> <td style="border: none;">Finishing ☐</td> <td style="border: none;">Rec/Store/Packaging ☐</td> <td style="border: none;">Other ☐</td> </tr> <tr> <td style="border: none;">Large Fab ☐</td> <td style="border: none;">Composite ☐</td> <td style="border: none;">Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐	
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																						
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																						
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																						
Large Fab ☐	Composite ☐	Supplier ☐																							
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval																		
Description Work Order Deviation				Disposition			Completed By																		
							Lead hand / Supervisor Approval Verification																		
							QC / QA Coordinator Approval																		
Root Cause		FAULT CATEGORY																							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : ☐																		

SPECIFICATION CONTROL DRAWING

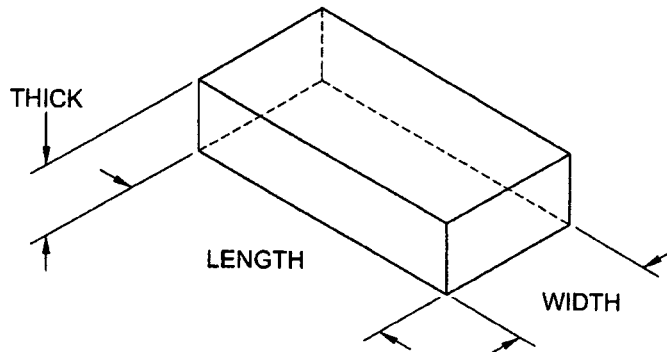

PURCHASE MATERIAL ACCORDING TO THE FOLLOWING TABLE. SPECIFY ALLOY, LENGTH x WIDTH x THICK (+0.030/-0.000), AND GRAIN DIRECTION AS SHOWN.

TOLERANCES ON ALL DIMENSIONS ARE +0.030/-0.000.

ALL DIMENSIONS ARE IN INCHES.

B ACCEPTABLE SPECIFICATIONS FOR 7075-T7351 ALUMINUM ARE AMS-QQ-A-250/12, QQ-A-250/12, OR ASTM B209

Part No.	Alloy	Length	Width	Thick	Grain Direction
D6101-001	7075-T7351 (QQ-A-250/12)	6.000	6.250	2.000	Along 6.000 Length
D6101-003	7075-T7351 (QQ-A-250/12)	7.875	6.250	2.000	Along 7.875 Length
D6101-005	7075-T7351 (QQ-A-250/12)	5.000	8.250	2.500	Along 5.000 Length
D6101-007	7075-T7351 (QQ-A-250/12)	7.750	8.250	2.500	Along 7.750 Length
D6101-009	7075-T7351 (QQ-A-250/12)	8.700	8.250	2.500	Along 8.700 Length
D6101-011	7075-T7351 (QQ-A-250/12)	9.700	8.250	2.500	Along 9.700 Length
D6101-013	7075-T7351 (QQ-A-250/12)	10.100	8.250	2.500	Along 10.10 Length
B D6101-015	7075-T7351 (QQ-A-250/12)	9.450	6.250	2.500	Along 9.450 Length
D6101-017	7075-T7351 (QQ-A-250/12)	6.350	6.250	2.250	Along 6.350 Length

RELEASED
09/07/15/W

136767 MJS
1509-04

B	ADDED D6101-015/-017, ADD ASTM B209	RF	09.04.23
A	NEW ISSUE	CP	01.03.30
REV.	DESCRIPTION	BY	DATE
DESIGN	CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	<i>[Signature]</i>	DRAWING NO.	REV. B
MFG. APPR.	<i>[Signature]</i>	D6101	SHEET 1 OF 1
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	SADDLE BILLET, 7075	NTS
DATE	09.04.23	COPYRIGHT © 2001 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID **PO29713**

Purchase Order Date 9/8/2015

PO Print Date 9/8/2015

Page Number 2 of 3

Order From :

METAUX CASTLE
P.O. BOX 4090 STN A
TORONTO, ONTARIO M5W OE9
CANADA

VU-MET002

Ship To : DART AEROSPACE LTD

1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name

Vendor Phone

Ship To Contact

Ship To Phone

Ship Via:

Yours ppd

Ship Acct:

Buyer

Chantal Lavoie

Customer POID

Customer Tax #

10127-2607

Terms

Net 30

Currency

USD

FOB

Destination-Collect

Line Total: \$855.00

3	D6101-007P	7075-T7351 8.25X7.75X2.5	9/24/2015	40.00	\$61.10	\$2,444.00
---	------------	-----------------------------	-----------	-------	---------	------------

Yes

Each

9/24/2015

AS PER DWG D6101 REV. B

B136766

MATERIAL: 7075-T7351 (QQ-A-250/12)

SIZE: 7.750" X 8.250" X 2.50" THICK

GRAIN DIRECTION ALONG: 7.750" LENGTH

TOLERANCE AS PER QUOTE +.030"/-.000"

Line Total: \$2,444.00

4	D6101-017P	ALUM BILLET	9/24/2015	10.00	\$64.75	\$647.50
---	------------	-------------	-----------	-------	---------	----------

Yes

Each

9/24/2015

AS PER DWG D6101 REV. B

B136767

SIZE: 6.350" X 6.250" X 2.250" THICK

GRAIN DIRECTION ALONG 6.350" LENGTH

MATERIAL: 7075-T7351 QQ-A-250/12

TOLERANCE AS PER QUOTE +.030"/-.000"

Line Total: \$647.50

Note:

9/8/2015

2015-09-23

**Castle Metals®**

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 1 of 2

Shipment No:2733780

Ship From: A. M. Castle & Co. TORONTO - CASTLE METALS 2150 ARGENTIA ROAD MISSISSAUGA, ON L5N 2K7		Sold To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA		Ship To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CAN		Deliver To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA	
Date Shipped 22-SEP-2015	F.O.B. ORIGIN	Freight Terms Prepaid		Carrier MANITOULIN		BOL No 2733780-2	

Shipment Details	Final Destination Branch - TOR
-------------------------	---------------------------------------

Order No 4050922	Line No 3	Item No 750704.MO	Description 2.2500.PL.7075.T7351.ALUMINUM.USI.48.5000.144.5000 CUT 2SIDED TO 6.25 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6.35")) X 6.35 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6.35")) - ALUMINUM PLATE SAW SPECIFICATIONS: AMS-QQ-A-250/12				
Purchase Order No 29713	Part Number YOUR ITEM NUMBER: D6101-017		Ordered Qty 10.00 PCS		Invoice Qty 10.00 PCS		
Details			ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #'S SHIP TO CASTLE, MONTREAL (POINTE-CLAIRE) CUSTOMS BROKER: GEORGE H. YOUNG END USER: DART AEROSPACE END USE: COMMERCIAL AIRCRAFT PARTS				
Delivery No. 120176397	Mill KAISER ALUMINUM	Heat Number 	Mech Id	PCS 10 ✓	Width (IN)	Length (IN)	Shipped Qty(LBS) 91.9537



Castle Metals®

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 2 of 2

These commodities/technologies are subject to US Export Administration & US State Dept. Regulations and, if intended for export, were/are exported thereunder. Diversion contrary to US Law is Prohibited.

We hereby certify the material covered by this certification conforms in accordance with the above specifications and has been found to meet the applicable requirements for the material, including any specifications forming a part of the description. Test reports are on file subject to examination. All claims for defective material are waived unless made in writing to A.M. Castle & Co. within 60 days of the shipment. Material cut to the correct size, or material cut by the customer cannot be returned for credit.

Reviewed by Authorized Castle Metals Representative:

Date:

Name:

SEP 22 2015



881509-23

SHIP TO:

A M CASTLE & CO
14001 ORANGE AVE
P.O. BOX 1402
PARAMOUNT, CA 90723

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

SOLD TO:

AM CASTLE & CO- SOLD TO
1420 KENSINGTON RD
SUITE 220
OAK BROOK, IL 60523

CERTIFIED TEST REPORT

Serial Number

4362544

CUSTOMER PO NUMBER: 313064		WORK PACKAGE: 750704		CUSTOMER PART NUMBER:		SHIP RUN/LOAD: 103113/18		GOV'T CONTRACT NUMBER:		
KAISER ORDER NO: 1184008		LINE ITEM: 1	SHIP DATE: 29-JAN-2015		ALLOY: 7075	CLAD: BARE	TEMPER: T7351	PRODUCT DESCRIPTION: KaiserSelect Plate		
WEIGHT SHIPPED: 4888 LB		QUANTITY: 3 PCS EST.		TRUCK B/L #: 2052101		GAUGE: 2.2500 IN (57.1500 MM)		DIAMETER/WIDTH: 48.500 IN (1231.9 MM)		LENGTH: 144.500 IN (3670.3 MM)

MHU 1859709: LOT 120483B3/3 pieces;

DAS
14
9-89

Certified Specifications

AMS 4078/RevJ
ASTM B 209/Rev14
BSS 7055/RevB
DPS 4.713/RevAK
GSS16100/RevG/Amd1

AMS-QQ-A-250/12/RevA
ASTM B 594/Rev13
CMMP 025/RevU
EAC MS1011/RevE
MMS 159/RevT

AMS-STD-2154/RevA
BAC 5439/RevJ
CSTI 006/RevE
GAMPS 9101/RevB/AmdSCN1
PS 21211/RevM

Test Code: 4297

Test Results

Lot: 120483B3 Cast 730

Drop 06

Ingot 2



Melted in USA

(ASTM E8/B557)
(EN 2002-1)

Tensile:	Temper T7351	Dir / # Tests LT / 2 (Min:Max)	Ultimate KSI (MPA) 70.0 : 71.9 (483 : 496)	Yield KSI (MPA) 59.6 : 61.4 (411 : 423)	Elongation % 11.4 : 11.8
----------	-----------------	-----------------------------------	--	---	-----------------------------

(ASTM E1004)
(EN 2004-1)

Conductivity %IACS :	40.3 Min	40.9 Max
(MS/M) :	23.4 Min	23.7 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.08	0.20	1.5	0.06	2.4	0.19	5.6	0.03	0.01	0.01	TOT 0.05

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4362544

ALLOY LIMITS

	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER	MAX
7075												
MIN(wt%)	0.00	0.00	1.2	0.00	2.1	0.18	5.1	0.00	0.00	0.00	EACH	0.05
MAX(wt%)	0.40	0.50	2.0	0.30	2.9	0.28	6.1	0.20	0.05	0.05	TOT	0.15

Aluminum Remainder

ORDER COMMENTS

AMC CA-15413B R 6
AMS 4078,AMS QQ-A-250/12,AMS STD-2154,A
STM B209,ASTM B594,BS
S 7055,CMMP 025,CSTI 006,DPS 4.713,GAMP
S 9101,MMS 159,PS 212

11


TEST NOTES

Metal represented by this test report was 100% immersion
ultrasonically tested from one side with 3mm dead zones top
and bottom and meets the Class A and Class B requirements of
all specifications referenced on this test report. No
surface marking of sonic indications is performed.

CERTIFICATION

Kaiser Aluminum Fabricated Products, LLC (Kaiser), is ISO-9001:2008/AS9100C certified and hereby certifies that all material shipped under this order:

- * has been inspected, tested, and found to be in conformance with the requirements of the specifications indicated herein. For material thicknesses outside specification limits, mechanical properties are as shown herein and chemical composition meets specification requirements.
 - * was melted in the United States of America or a qualifying country per DFARS 225.872-11(a), was manufactured in the United States of America, and meets the requirements of DFARS 252.225 for domestic content.
 - * has been thermally processed in compliance with AMS 2772, where applicable.
 - * is mercury free, within the limits of detection of ASTM E1251 (≤ 1 ppm).
 - * is in compliance with RoHS 2, European Union Directive 2011/65/EU.
 - * is in compliance with and regularly monitors any updates to the European Chemical Agency, ECHA, REACH regulations, (EC) n°1907/2006.
 - * is free of Conflict Minerals, as defined in Section 15.2 of the Dodd-Frank Act.
- Any warranty is limited to that shown on Kaiser Aluminum's standard general terms and conditions of sale. Test reports are on file, subject to examination. Test reports shall not be reproduced except in full, without the written approval of the Kaiser Aluminum laboratory. The recording of false, fictitious or fraudulent statements or entries on the certificate may be punished as a felony under federal law.



JAMES HEMENWAY, LABORATORIES SUPERVISOR

MATERIAL RECEIPT INSPECTION FORM

MATERIAL: D6101-617
 DATE: 15/09/24

PO / BATCH NO: 29713/136767

MATERIAL CERT REC'D: yes
 QUANTITY RECEIVED: 10
 QUANTITY INSPECTED: 10
 QUANTITY REJECTED: _____

THICKNESS ORDERED: 6.350X6.25X2.25
 THICKNESS RECEIVED: 6.350X6.25X2.290
 SHEET SIZE ORDERED: _____
 SHEET SIZE RECEIVED: _____

DESCRIPTION	NCR (Check Y/N)	COMMENTS
SURFACE DAMAGE	Y ☒	
CORRECT FINISH	☒ N	
CORROSION	Y ☒	
CORRECT GRAIN DIRECTION	☒ N	
CORRECT MATERIAL	☒ N	
CORRECT THICKNESS	☒ N	
PHOTO REQUIRED	Y ☒	
CORRECT MATERIAL	☒ N	
CORRECT REF # TO LINK CERT	☒ N	
CORRECT MATERIAL IDENTIFICATION	☒ N	
CORRECT M# ON THE MATERIAL	☒ N	
DOES THIS MATERIAL REQUIRE ENGINEERING SIGN OFF	Y ☒	
DOES THIS REQUIRE AN EXTRUSION REPORT	Y ☒	

CUT SAMPLE PIECE OF MATERIAL AND PERFORM A HARDNESS CHECK. RECORD RESULTS BELOW					
TYPE OF MATERIAL SIZE OF TEST SAMPLE HARDNESS / DUROMETER READING	HRC	HRB	DUR A	DUR D	

testers located in the Quality Office

QC 18 INSPECTION		ENGINEERING SIGNOFF (if required)
INSPECTED BY: <u>DAS</u> <u>14</u> DATE: <u>15/09/24</u>	SIGNED OFF BY: _____ DATE: _____	

Attach this inspection sheet with the corresponding material cert and remit to be scanned and received in

MATERIAL RECEIPT INSPECTION FORM

INSTRUCTIONS FOR INSPECTING BAR, TUBING, ROUND, & SHEET STOCK

- 1- VERIFY STOCK TO DART PURCHASE ORDER
- 2- MEASURE ALL DIMENSIONS FOR EACH PURCHASED STOCK
 - a WIDTH, THICKNESS, DIAMETER, WALL THICKNESS & LENGTH
- 3- VERIFY CONDITION OF MATERIAL i.e. DAMAGED, CORRODED, etc
- 4- VERIFY THAT SUPPLIER HAS A NUMBER (HEAT #) ON ITS RECEIVING REPORT TO LINK TO MATERIAL CERTS
- 5- VERIFY MATERIAL CERTS ARE CORRECT TO THE DART PO INSTRUCTIONS
- 6- REMOVE / CUT A PIECE OF MATERIAL FOR SAMPLE HARDNESS TESTING

INSTRUCTIONS FOR INSPECTING SKIDTUBE & STEP EXTRUSION

- 1- VERIFY TO DART SUPPLIED DRAWING
- 2- SAMPLE INSPECT MATERIAL IN BUNDLE TO ENSURE MATERIAL CAN BE RECEIVED INTO DART
- 3- USING PORTABLE HARDNESS TESTER VERIFY HARDNESS OF THE MATERIAL TO THE DRAWING
- 4- VERIFY THAT MATERIAL CERTS MATCH TO WHATS CALLED UP ON THE DART DRAWING

AFTER MATERIAL PASSES INSPECTION

- 5- HAVE DART EMPLOYEES START STOCKING MATERIAL BUT REQUEST MIN 20pcs FOR FULL INSPECTION
- 6- INSPECT ALL DIMS AS PER DRAWING REQUIREMENTS

INSTRUCTIONS FOR INSPECTING CROSS TUBE MATERIAL

- 1- VERIFY MATERIAL CERTS MATCH THE REQUIREMENTS ON THE DART DRAWINGS
- 2- INSPECT MIN HALF THE BATCH OF EXTRUSION RECEIVED INTO DART
- 3- INSPECT MATERIAL AS PER THE EXTRUSION REPORT
 - a WALL THICKNESS USING ULTRA-SONIC IN 4 LOCATIONS
 - b OUTSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - c INSIDE DIAMETER HIGHEST/LOWEST BOTH ENDS
 - d STRAIGHTNESS @ CENTER OVER 12" SPAN
 - e WALL THICKNESS USING TUBE MICROMETER HIGHEST/LOWEST BOTH ENDS
- 4- IDENTIFY EACH TUBE IN SEQUENCE OF INSPECTING (TUBE 1, TUBE 2,) AND W/O# AND PO#
- 5- RECORD ALL FINDINGS ON EXTRUSION REPORT

IF ANY QUESTIONS PLEASE SEE QC COORDINATOR BEFORE GOING FURTHER
